


GZA GeoEnvironmental, Inc.

Project: Schedule Update

Critical — Work by Others — Summary Deadline ◆
 Noncritical — Milestone ◆ External Milestone ◇

ID	Task Name	Duration	Start	Finish	June 2019	July 2019	August 2019	September 2019	October 2019	November 2019	December 2019	January 2020	February 2020	March 2020	April 2020
					5/26 6/2 6/9 6/16 6/23 6/30	7/7 7/14 7/21 7/28	8/4 8/11 8/18 8/25	9/1 9/8 9/15 9/22 9/29	10/6 10/13 10/20 10/27	11/3 11/10 11/17 11/24	12/1 12/8 12/15 12/22 12/29	1/5 1/12 1/19 1/26	2/2 2/9 2/16 2/23	3/1 3/8 3/15 3/22 3/29	4/5 4/12 4/19 4/26 5/3
52	Backfill Cr Area	2 days	11/18/2019	11/19/2019											
53															
54	DCC Areas South of Rum Creek	10 days	11/19/2019	12/4/2019											
55	DCC areas excavation	2 days	11/19/2019	11/20/2019											
56	DCC verification sampling & lab analysis	5 days	11/20/2019	11/26/2019											
57	DCC areas backfill/restoration	1 day	11/27/2019	11/27/2019											
58	South Side of Rum Creek Restoration	3 days	12/2/2019	12/4/2019											
59	South Side of Rum Creek Complete	0 days	12/4/2019	12/4/2019											
60															
61	Spring Planting	15 days	3/2/2020	3/20/2020											
62	Final Riverbank Restoration	15 days	3/2/2020	3/20/2020											
63	Tannery Remediation Complete	0 days	3/20/2020	3/20/2020											

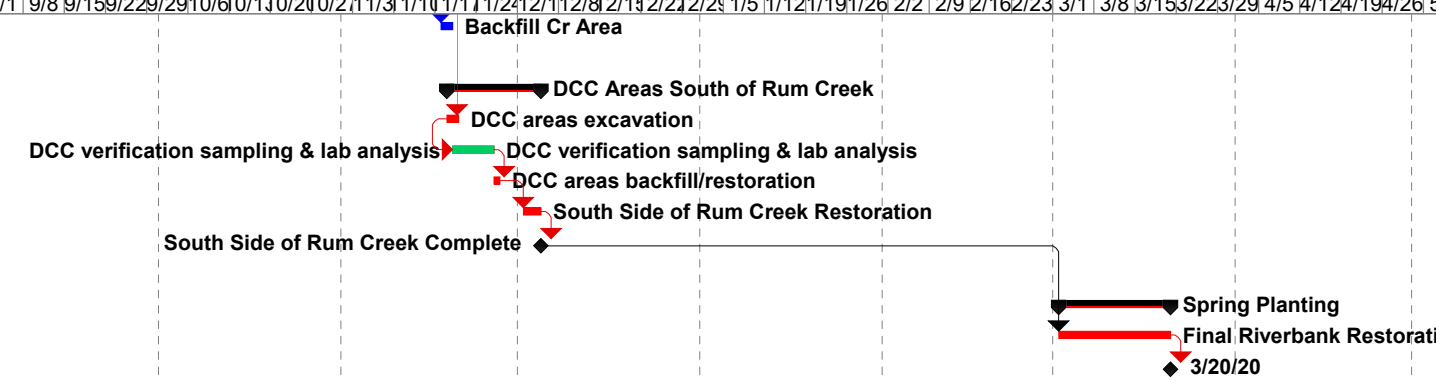

Critical — Work by Others — Summary Deadline +
 Noncritical — Milestone ◆ External Milestone ◇
